


16.05.2025		
Contractul de lucrări Nr. RSP/W15/04: Construction of M3 Slobozia Mare Bypass, km 0+000 - km 16+598 (remaning works)		
Invitație pentru depunerea ofertelor (data) Invitation to tender (date)	14.06.2024	
Finanțare Funding	European Bank for Reconstruction and Development (EBRD), EBRD Project ID: 45094	
Lungimea sectorului de drum (km) The length of the road sector (km)	16,6 km	
Antreprenor Contractor	Irinda Prim & Nouconst Joint Venture	
Inginer (Compania de Supervizare) Engineer	IRD Engineering	
Data semnării contractului Date of signing the contract	06.12.2024	
Înștiințarea de începere a lucrărilor	17.03.2025	
Durata de execuție a lucrărilor (luni)	365	
Extensie de timp acordată (zile) Extension of time (days)	0	
Termenul de finalizare al lucrărilor The deadline for the completion of the works	17.03.2026	
Timp utilizat (%) Time used (%)	16%	Lucrari raportate
Valoarea de Contract Acceptată (euro) Accepted Contract Value (EUR)	10 459 023.27 EUR	
Valoarea achitată până în prezent (EUR) Amount paid to date (EUR)	1 045 902.23 EUR	
Progresul financiar (%) Financial progress (%)	10.00%	
Progresul fizic (%) Physical progress (%)	0.00%	
Data ultimei sedinte cu Antreprenorul si Inginerul The date of the last meeting with the Contractor and the Engineer	-	
		Nu s-au executat lucrari in perioada raportata

Programme of Works No. 025 dated 11.09.2023

	Jan-25	Feb-25	Mar-25	Apr-25	May-25	Jun-25	Jul-25	Aug-25	Sep-25	Oct-25	Nov-25	Dec-25	Jan-26
Planned Progress													
Actual Progress													
Monthly Progress													
Time Elapsed	-12%	-5%	4%	12%	20%	29%	37%	46%	54%	62%	71%	79%	79%

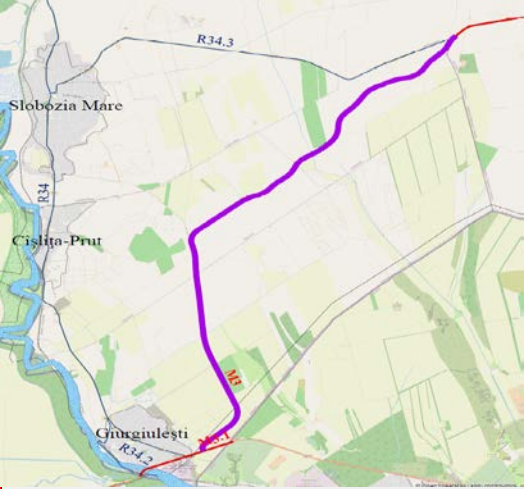
